AIRcoin — Product Requirements Document

Oct 10, 2026 · @omkar

1. Overview

AIRcoin pays people for growing pollution-absorbing plants. A low-cost camera "miner" watches up to 20 tagged plants and estimates the pollution they remove. It mints AIRcoin as proof of that useful work. Polluting companies must buy and burn AIRcoin to meet compliance, which creates demand.

Problem. Urban air pollution (PM2.5, PM10, NO_2, SO_2, CO, VOCs, CO_2) has no direct, verifiable incentive for citizens to fight it. Carbon credits target large projects and are hard for households to join.

Product in one line. A plant-monitoring miner, a token minted from verified plant work, and a marketplace where citizens sell the token and polluters buy and burn it.

Hackathon goal. Show a working end-to-end system on stage:

- A physical 20-plant rig with a real camera, Raspberry Pi and GPS.
- A live digital twin: camera feed with detections, a 3D model of the miner's insides, sensor gauges and a minting ticker.
- Live anti-cheat: removing a plant, adding a fake plant or reusing a sticker is caught on screen.
- Real miner software fed by simulated sensor data, minting real AIRcoin on a blockchain testnet.
- A wallet and marketplace where an owner sells AIRcoin and a company buys and burns it for compliance.

Users.

User	What they do
Miner owner (citizen, housing society, school)	Buys the miner, plants and tags up to 20 plants, earns and sells AIRcoin
Polluting company / factory	Buys AIRcoin and burns it to meet a compliance obligation
Regulator (government / pollution control board)	Sets obligations, registers miners, audits mints and burns

User	What they do
AIRcoin operator (our team)	Runs the validator, calibration and marketplace

2. Real-world system concept

This is the full product we pitch. Section 3 says which parts the hackathon builds for real.

2.1 The miner (hardware)

Part	Suggested component	Purpose
Compute	Raspberry Pi 4 (4 GB) or Pi 5	Runs vision, estimation and signing
Camera	Pi Camera Module 3 NoIR + blue filter (or standard Module 3)	Reads stickers, sizes plants; NoIR enables a plant-liveness (NDVI) check
GPS	u-blox NEO-6M / NEO-M8N over UART	Fixes the miner's location for anti-cheat and local AQI lookup
Wi-Fi	Pi on-board Wi-Fi	Sends telemetry and proofs
Air sensors	PMS5003 (PM2.5/PM10), MQ-135 (gas/VOC), SCD40 (CO_2), BME280 (temp/humidity/pressure)	Measures surrounding air; hackathon feeds simulated values
Security	Device key pair in a file (hackathon) / ATECC608 secure element (production)	Signs every proof so it can't be forged

2.2 The stickers

Each miner ships with 20 printed fiducial stickers (ArUco or AprilTag markers). Every sticker ID is registered to exactly one miner at sale time. A sticker seen by a different miner, or by its own miner at a new location, is rejected. This stops owners from moving the same plants between miners to mint twice.

2.3 The 20 prescribed plants

The owner plants up to 20 species from a fixed list chosen so that, together, the set targets every major pollutant (particulates, NO_2, SO_2, CO, VOCs such as benzene and formaldehyde, and CO_2). Each species has a calibrated coefficient per pollutant. The final list and coefficients are an open question owned by Workstream B.

2.4 Calibration

We estimate each species' uptake by placing it in a closed enclosure with known pollutant levels and measuring the drop over time, per unit of leaf area. The result is a coefficient table: species × pollutant → grams removed per m² of leaf per hour at a reference concentration. For the hackathon this table is seeded from published literature and labelled as an estimate.

2.5 Proof of Useful Work (minting)

1. The miner watches its plants continuously and identifies each tagged plant, its species, its visible leaf area and whether it is alive.
2. It reads ambient air quality (local sensors plus GPS-based AQI).
3. Every epoch it estimates pollution removed per plant using the calibration table.
4. It signs an attestation: miner ID, epoch, plant states, sensor summary, GPS, image hashes and the claimed amount.
5. A validator checks the signature, the sticker bindings, location and plausibility, then mints AIRcoin to the owner's wallet.

Estimation model (per plant i, per pollutant p, per epoch):

```
R_{i,p} = k_{s(i),p} \times A_i \times H_i \times f\left(\frac{C_p}
{C_{p,\mathrm{ref}}}\right) \times \Delta t
```

k = calibrated coefficient for species s, A = estimated leaf area, H = health/liveness score (0 to 1), C = ambient concentration, f = a capped concentration factor, Δt = epoch length. Pollutant amounts are weighted into one unit (for example 1 AIR = 1 g PM2.5-equivalent removed); the exact unit definition is an open question.

2.6 Marketplace and demand

- Owners sell AIRcoin on our marketplace for rupee-pegged test stablecoin.
- The regulator assigns each polluting company a yearly AIRcoin burn obligation based on its emissions.
- Companies buy AIRcoin and burn it through a compliance function that records which obligation it meets.
- Burning permanently removes supply, so steady obligations create steady demand. The government can later run the validator and registry itself.

3. Hackathon scope

Everything a judge sees working is real software; only the air sensors and the calibration data are simulated.


Component	In the demo	How
Camera, Raspberry Pi, GPS	Real	Physical rig facing the 20-plant setup
Sticker detection, plant ID, removal and fake-plant detection	Real	Live vision pipeline on the Pi (laptop fallback)
Air sensors (PM, gas, CO_2, temp, humidity)	Simulated	Sensor simulator with scenarios (clean day, traffic spike, Diwali smog) behind the same interface real sensors would use
Calibration coefficients	Literature-seeded estimates	Static table, versioned, clearly labelled as estimates
Miner software, estimation, signing	Real	Runs live on the Pi
Validator and minting	Real	Off-chain verifier + smart contracts on a public testnet (local chain as fallback)
AIRcoin, wallet, marketplace, compliance burn	Real	Testnet contracts + web apps
Digital twin (3D miner, live feed, dashboards)	Real	Web app
Government portal	Real, minimal	Regulator sets obligations, views burns

Out of scope for the hackathon: real enclosure calibration, production hardware and casing, secure-element key storage, mainnet deployment, KYC, payments in real money, mobile apps, legal and tax compliance for a traded token, and scaling beyond a handful of miners.

4. System architecture and interface contracts

The three workstreams meet only at four frozen interfaces (C1 to C4), so each person can build and test against mocks without waiting for the others.

Plant work flows from the camera to minted AIRcoin

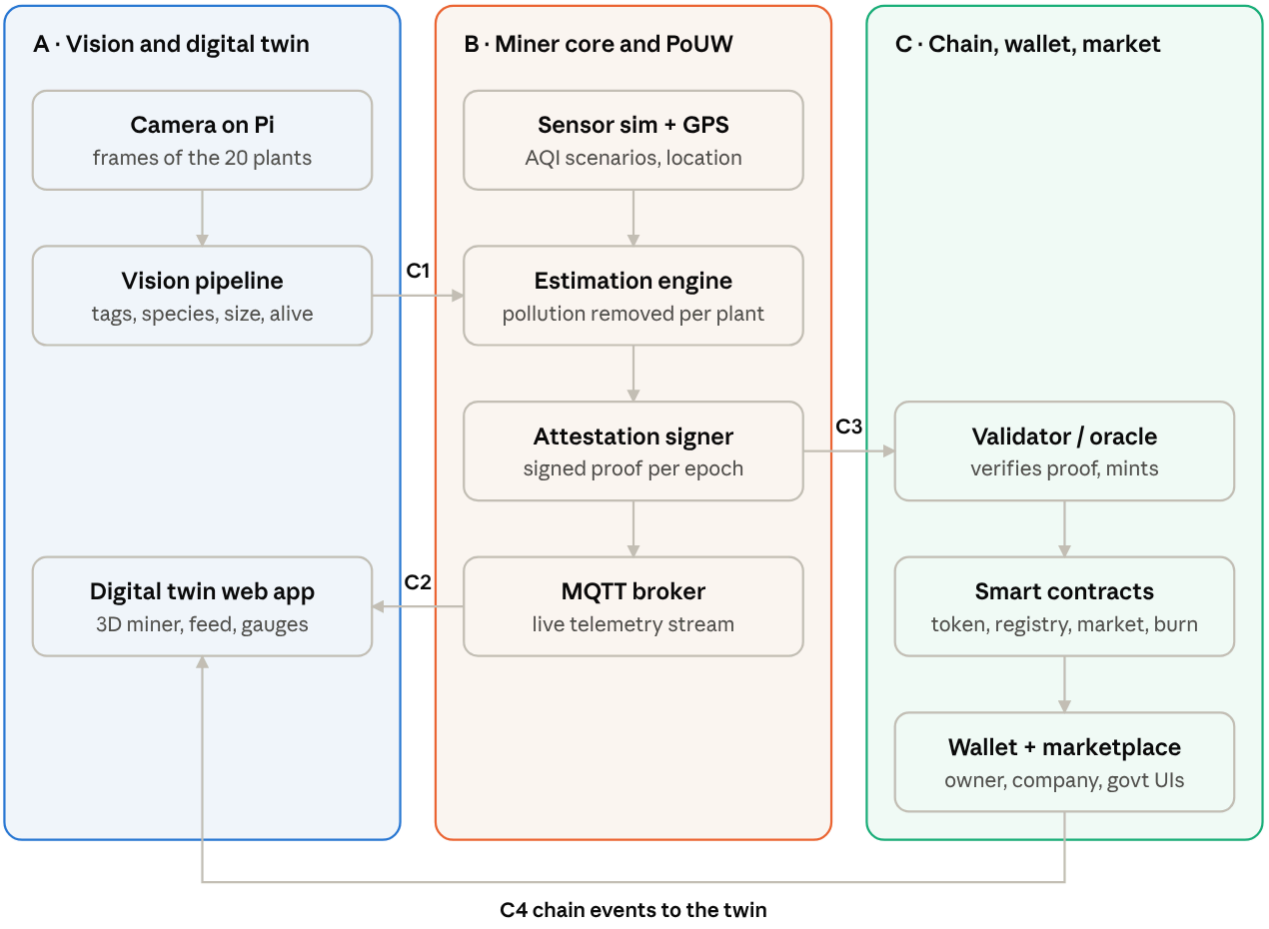

System architecture · 3 workstreams, 4 interface contracts

The camera feeds vision (A), vision and simulated sensors feed the estimator (B), signed proofs go to the validator (C), and chain events flow back into the twin.

4.1 Interface contracts

ID	From → To	Transport	Payload (v1)
C1	A → B	MQTT `miner/{id}/vision`, 1 message/s	`ts`, `frame_hash`, `plants[]`: `tag_id`, `species`, `species_conf`, `leaf_area_cm2`, `alive_score` (0–1), `bbox`, `status` (present / missing / suspect)

ID	From → To	Transport	Payload (v1)
C2	B → A	MQTT `miner/{id}/telemetry` (1/s) and `miner/{id}/epoch` (per epoch)	Sensor readings (PM2.5, PM10, CO_2, VOC index, NO_2, temp, humidity), GPS fix, per-plant estimate, epoch total, attestation status, anti-cheat flags
C3	B → C	HTTPS `POST /v1/attestations`	`miner_id`, `epoch`, `start`, `end`, `gps`, `sensor_summary`, `plants[]`, `amount`, `evidence_hash`, `signature` (secp256k1) → returns `status`, `tx_hash`, `reason`
C4	C → A and apps	REST + WebSocket	`GET /v1/miners/{id}`, `/balance`, `/mints`; live events `mint`, `transfer`, `trade`, `burn`


Shared data, owned jointly:

- **Miner and sticker registry** (JSON + on-chain): `miner_id`, device public key, owner wallet, the 20 `sticker_ids`, registered GPS location.
- **Species catalogue**: 20 species IDs, display names, reference images, pollutant coefficients (owned by B, read by A).
- **Signing**: secp256k1 (Ethereum-style) keys so the contract could verify proofs directly later.

Rules: the contracts are frozen as v1 at the end of Phase 1; any change needs all three to agree. Each workstream ships a mock emitter for the interface it produces in its first days, so nobody is blocked.

5. Global phase scope

The project runs in three phases; nobody starts the next phase until the whole team passes the gate. Suggested split of the available time: Phase 1 about 40%, Phase 2 about 35%, Phase 3 about 25%. The hackathon deadline is an open question, so phases are not dated yet.

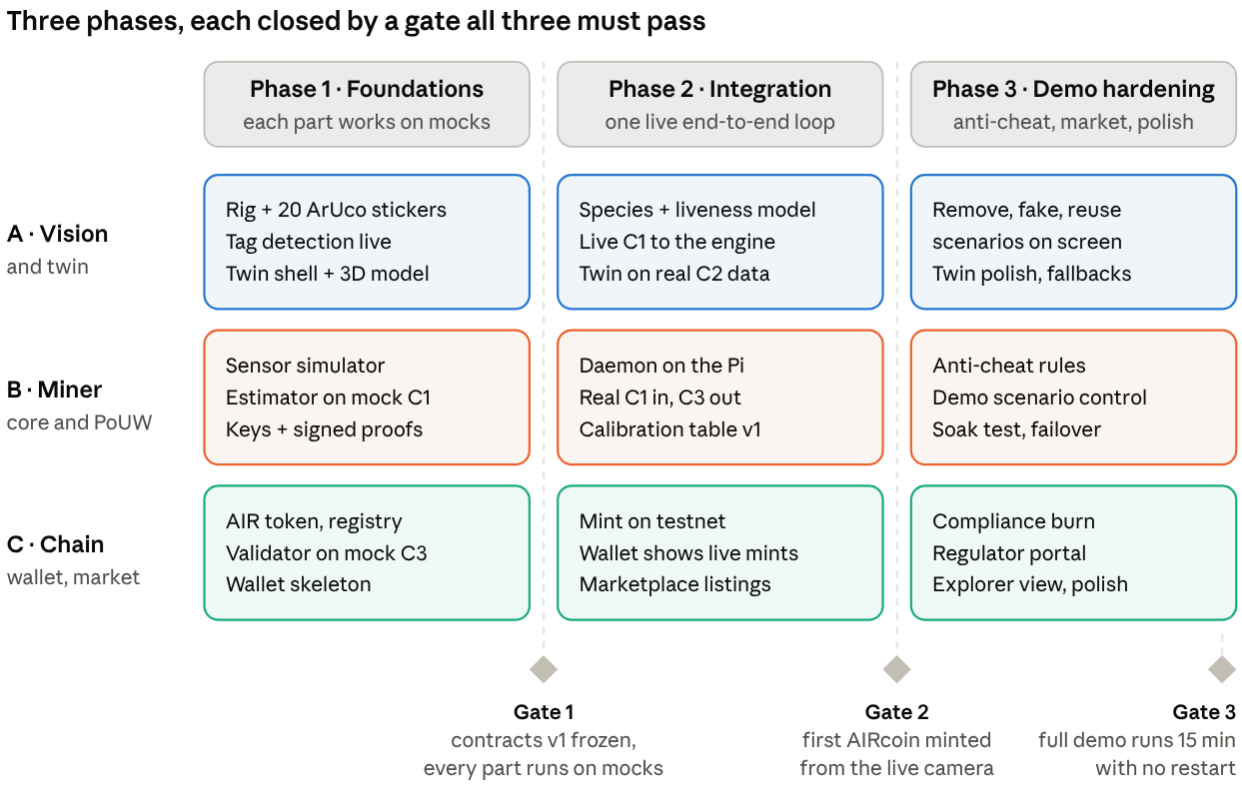

Global roadmap · 3 phases × 3 workstreams, 3 gates

Each cell is that person's headline for the phase; sections 7 to 9 give the full scope.

Phase 1 · Foundations (build alone, against mocks)

Goal: every component works on its own, with fake inputs shaped exactly like the real interfaces.

- Interface contracts C1 to C4, the registry schema and the species catalogue written and agreed on day 1.
- Each person ships a mock emitter for the interface they produce.
- Hardware rig assembled; camera, GPS and Pi working.
- Smart contracts deployed to a local chain; miner software runs on a laptop.

Gate 1 exit criteria:

- [ ] C1–C4 schemas frozen as v1 in the repo
- [ ] Vision detects all 20 stickers in a still frame
- [ ] Estimator turns mock C1 + simulated sensors into a signed attestation
- [ ] Validator accepts a valid mock attestation and rejects a tampered one on the local chain
- [ ] Twin page loads the 3D miner model and renders mock C2 data

Phase 2 · Integration (one live loop)

Goal: a real plant in front of the real camera produces a real AIRcoin that shows up in the wallet and the twin.

- Mocks replaced by live components one interface at a time (C1, then C3, then C2 and C4).
- Miner daemon runs on the Raspberry Pi; contracts move to a public testnet.
- Calibration table v1 and the estimation model are in place.

Gate 2 exit criteria:

- [ ] Camera → vision → estimator → signed proof → validator → mint works with no manual step
- [ ] Minted amount appears in the owner wallet and on the twin within 60 s of epoch close
- [ ] Removing a plant lowers the next epoch's mint
- [ ] Owner can list AIRcoin for sale on the marketplace

Phase 3 · Demo hardening (the story on stage)

Goal: every claim in the pitch is shown live, and nothing breaks during a 15-minute demo.

- Anti-cheat scenarios: plant removed, fake plant added, sticker reused on a second miner, miner moved.
- Full market loop: owner sells, company buys and burns, regulator sees the obligation met.
- Demo scenario controller, fallbacks (recorded video, local chain, laptop vision) and a rehearsed script.

Gate 3 exit criteria:

- [ ] All demo steps in section 10 pass three rehearsals in a row
- [ ] Each fallback tested by switching it on mid-demo
- [ ] Pitch deck and a 2-minute backup video recorded

6. Team split

Each person owns one vertical slice end to end, from code to its part of the demo. They share nothing but the interface contracts in section 4.

Workstream	Owner	Owns	Produces	Consumes	Main skills
A · Vision and digital twin	Person 1 (TBD)	Hardware rig, stickers, computer vision, live feed, 3D miner model, twin dashboard	C1	C2, C4	Python, OpenCV, PyTorch/YOLO, React, Three.js, Blender
B · Miner core and PoUW engine	Person 2 (TBD)	Miner daemon, sensor simulator, GPS, calibration table, estimation model, device keys and signing, anti-cheat rules, MQTT broker, demo scenario controller	C2, C3	C1	Python, MQTT, data modelling, cryptography basics, Linux on Pi
C · Token, wallet and marketplace	Person 3 (TBD)	Smart contracts, validator and mint oracle, wallet, marketplace, company burn flow, regulator portal	C4	C3	Solidity, Hardhat/Foundry, ethers.js, Node.js, React

Working agreements:

- One monorepo with folders `vision-twin/`, `miner-core/`, `chain-market/` and a shared `contracts-schema/` folder for C1–C4 JSON schemas.
- Daily 15-minute sync: what's done, what's blocked, any contract change request.
- Integration happens only at gates; between gates each person tests against the others' mocks.
- Shared UI style (colours, fonts) so the twin, wallet and marketplace look like one product.

7. Workstream A · Vision and digital twin (Person 1)

Mission: make the miner see. Detect every tagged plant, prove it is the right species and alive, and show all of it live in a digital twin judges can explore.

Stack: Raspberry Pi 4/5, Pi Camera Module 3 (NoIR variant if the liveness check uses NDVI), Python, OpenCV (`cv2.aruco`), Ultralytics YOLOv8n-cls or MobileNetV3 for species, React + Vite, react-three-fiber (Three.js), Blender → glTF, Leaflet for the map, MQTT over WebSockets.

7.1 Components

1. **Physical rig.** A board with 20 pot slots in a 4 × 5 grid, camera on a fixed mount 1 to 1.5 m away so all 20 stickers are readable in one frame. One plastic plant and one spare sticker kept aside for the anti-cheat demo.
2. **Stickers.** ArUco markers (4×4 or 5×5 dictionary), IDs 0–19 for this miner, printed 4–5 cm on waterproof labels and fixed to a stake at the plant's base. Known marker size doubles as a scale reference for measuring plant size.
3. **Tag detection.** Detect and decode all markers each frame; match IDs against the miner's registered sticker set. Unknown IDs are flagged.
4. **Species identification.** For each tag, crop the region above it and classify it into one of the 20 species plus a "fake / not a plant" class. Training data: 100–200 photos per species from the rig plus public images. Flag a mismatch when the predicted species differs from the species registered to that tag.
5. **Plant size.** Segment green pixels in the crop (HSV threshold or excess-green index), convert to cm² using the marker's known size. Smooth over time.
6. **Liveness (fake-plant check).** Primary: NDVI from the NoIR camera with a blue filter (living leaves reflect near-infrared; plastic does not). Fallback: the classifier's fake class plus texture and colour variance and tiny frame-to-frame leaf motion. Output `alive_score` 0–1.
7. **Status machine.** Per tag: present → missing after 10 s unseen → removed after 60 s; suspect when species mismatches or `alive_score` is low. Debounced so a hand passing in front doesn't trigger alerts.
8. **Live feed.** Annotated stream (boxes, tag IDs, species, status colour) at about 15 fps, 720p, via MJPEG or WebRTC. Inference runs at 1–2 Hz.
9. **Digital twin web app.**
   - 3D miner model built in Blender: case, Raspberry Pi, camera, GPS module, sensor boards, wiring. Exploded view on click; each part shows its live reading.
   - Virtual 20-slot plant grid mirroring the rig: green = healthy, grey = missing, red = suspect.
   - Live camera panel, sensor gauges and AQI chart (from C2), mint ticker and wallet balance (from C4), anti-cheat event log, GPS pin on a map.

7.2 Phase scopes

Phase 1 · Foundations

- Assemble rig, mount camera, confirm Pi, camera and GPS work.
- Print stickers; tag detection working on still frames and live video.
- Start collecting species photos from the rig.

- Twin app skeleton: layout, 3D model v1 loaded, panels wired to the C2 and C4 mocks.
- Ship a C1 mock emitter (replays a recorded scene, can simulate a removed or fake plant).

- [ ] 20 of 20 stickers detected at the rig distance in normal room light
- [ ] 3D miner model renders in the browser and rotates smoothly
- [ ] Twin shows mock sensor and mint data updating every second

Phase 2 · Integration

- Train and deploy the species classifier; leaf-area estimation; liveness score.
- Publish real C1 messages from the Pi to the broker.
- Twin switches from mocks to real C2 and C4; live annotated feed embedded.

- [ ] Species top-1 accuracy at least 85% on held-out rig photos
- [ ] Removed plant shown as missing on the twin within 10 s
- [ ] Vision runs at 1 Hz or faster on the Pi (or on a laptop as declared fallback)
- [ ] Twin's coin ticker moves when C mints for this miner

Phase 3 · Demo hardening

- Tune fake-plant detection with the plastic plant under demo lighting.
- Anti-cheat alerts rendered clearly: banner, slot turns red, log entry, mint rate drop.
- Exploded-view animation, polish, dark mode for projectors.
- Fallbacks: vision on a laptop with a USB camera; recorded feed if the camera fails.

- [ ] Fake plant flagged in at least 4 of 5 tries
- [ ] Twin runs 15 minutes with no reload

Owns in the demo: steps 1–5 of the demo script (rig, twin, detection, removal, fake plant).

8. Workstream B · Miner core and PoUW engine (Person 2)

Mission: turn what the miner sees and senses into a trustworthy, signed claim of pollution removed. This is the "useful work" in Proof of Useful Work.

Stack: Python 3.11 asyncio daemon on Raspberry Pi OS, Mosquitto MQTT broker, gpsd / pynmea2 for GPS, `eth-account` or `coincurve` for secp256k1 signing, SQLite for the local log, systemd for auto-start, a small FastAPI panel for the scenario controller.

8.1 Components

1. **Sensor layer.** One driver interface per sensor (PM, gas/VOC, CO_2, NO_2, temp/humidity). The hackathon uses simulated drivers; real PMS5003, MQ-135, SCD40 and BME280 drivers can drop in later without other code changing.

2. **Sensor simulator.** Daily curves plus noise, with correlated values (PM10 tracks PM2.5, humidity affects PM). Named scenarios: clean morning (AQI about 50), rush hour (about 180), festival smog (about 400), rain washout. Switchable live.
3. **GPS service.** Reads the real GPS module; falls back to a fixed demo location indoors where there's no fix. Reports location and fix quality.
4. **Vision subscriber.** Consumes C1 and keeps the latest state of each of the 20 plants.
5. **Species catalogue and calibration table.** 20 species × pollutants coefficient table, seeded from published studies, versioned; its hash goes into every attestation. B owns choosing the final 20 species with the team.
6. **Estimation engine.** Applies the model in section 2.5 per plant per epoch. Caps per plant and per epoch. Missing plants count zero; suspect plants count zero and raise a flag.
7. **Epoch manager.** Epoch = 60 s in demo mode (with a time-acceleration switch), 1 hour in production.
8. **Attestation signer.** Builds the C3 payload, hashes the evidence (frame hashes + sensor readings + plant states + GPS), signs with the device key. Keys generated on first boot and registered with C's registry.
9. **Uplink.** Posts C3 with retry and an offline queue so no epoch is lost if Wi-Fi drops.
10. **Telemetry.** Publishes C2 every second and every epoch.
11. **Device-side anti-cheat flags.** Unknown sticker, species mismatch, low liveness, GPS more than 50 m from the registered spot, frozen camera (identical frame hashes), too many plants appearing at once, clock drift.
12. **Scenario controller.** A web panel for the demo: change AQI scenario, speed up time, simulate moving the miner, reset.
13. **Calibration protocol (document).** How the real enclosure test would work: sealed box, reference sensor, controlled pollutant source, decay measured with and without each species, coefficients fitted per m² of leaf. Used in the pitch to answer "how do you know?"

8.2 Phase scopes

Phase 1 · Foundations

- Write C1, C2, C3 schemas with A and C; publish mock C2 and mock C3 emitters.
- Sensor simulator with at least three scenarios.
- Estimator and epoch manager running on a laptop against the C1 mock.
- Key generation and signing; signature verified by a test script.
- Draft list of 20 species and coefficient table v0 with sources.

☐ One command produces a valid signed attestation from mock inputs

- [ ] Changing the scenario changes the estimate in the expected direction
- [ ] Tampering with any field makes the signature check fail

Phase 2 · Integration

- Daemon runs on the Pi as a systemd service; real GPS read.
- Consumes live C1 from A; posts live C3 to C′s validator; serves live C2 to the twin.
- Calibration table v1 frozen and documented.

- [ ] Live epochs every 60 s with no manual step for 30 minutes
- [ ] Unplugging Wi-Fi for 2 minutes loses no epochs (queued and sent later)
- [ ] Removing a plant lowers the next epoch′s estimate by that plant′s share

Phase 3 · Demo hardening

- All device-side anti-cheat flags working and visible in C2.
- Scenario controller panel used in rehearsals.
- Two-hour soak test on the Pi; watch CPU temperature and memory.
- Calibration protocol written up as a one-pager for judges.

- [ ] Each anti-cheat flag reproduced on demand
- [ ] Soak test finishes with no crash and no missed epoch

Owns in the demo: step 3 (AQI spike raises the mint rate) and the "how we calculate" explanation.

9. Workstream C · Token, wallet and marketplace (Person 3)

Mission: make AIRcoin a real token on a blockchain: minted only from verified proofs, held in a wallet, traded on a market, and burned by polluters for compliance.

Stack: Solidity + OpenZeppelin, Hardhat or Foundry, an EVM testnet (Polygon Amoy or Sepolia) with a local Hardhat chain as fallback, Node.js + TypeScript validator service, ethers.js, React + Vite for the web apps, SQLite or Postgres for indexing.

9.1 Smart contracts

Contract	Key functions	Rules
`AIRToken`	ERC-20, `mint`, `burn`	Only the mint controller can mint; no admin mint

Contract	Key functions	Rules
`MinerRegistry`	`registerMiner(minerId, deviceAddr, owner, stickerSetHash, geohash)`, `revoke`	Only the registrar (operator or regulator) registers; each sticker belongs to one miner
`MintController`	`mintForEpoch(minerId, epoch, amount, evidenceHash, sig)`	Verifies the device signature on-chain (`ecrecover`); one mint per miner per epoch; per-epoch cap
`Marketplace`	`list(amount, price)`, `buy(id)`, `cancel(id)`	Escrow of AIR; paid in `tINR`, a mock rupee stablecoin with a faucet
`ComplianceRegistry`	`setObligation(company, period, amount)`, `burnForCompliance(period, amount)`	Regulator sets obligations; burns are recorded against them and can't be undone

9.2 Off-chain services and apps

1. **Validator / mint oracle.** Receives C3, then checks: signature matches the registered device; miner is active; every sticker belongs to this miner and wasn't claimed by another miner in the same window (the cross-miner duplicate check); GPS inside the registered geofence; amount within the plausibility cap for those species and that AQI; epoch not already minted. Passes → sends `mintForEpoch`; fails → stores the rejection reason.
2. **Indexer + C4 API.** Listens to contract events; serves balances, mint history, trades and burns over REST and WebSocket.
3. **Wallet.** Connect MetaMask, or a built-in demo wallet for judges. Shows AIR and tINR balances, per-miner mint history, send/receive with QR codes.
4. **Marketplace.** Listings, buy flow, price and volume chart, recent trades.
5. **Company portal.** Obligation progress bar, "buy and burn" in one flow, a burn certificate with the transaction hash.
6. **Regulator portal.** Register miners and sticker sets, set obligations, see total minted vs burned, review rejected and flagged attestations.

9.3 Phase scopes

Phase 1 · Foundations

- All five contracts written with unit tests; deployed on a local chain.
- Validator running against the C3 mock from B.
- Wallet skeleton reading local-chain balances; C4 mock emitter for A.

- [ ] Valid mock attestation mints; tampered, replayed or over-cap ones are rejected
- [ ] Contract test coverage on mint, burn and escrow paths
- [ ] Wallet shows a balance change after a local mint

Phase 2 · Integration

- Contracts deployed and verified on the public testnet; demo miner registered with its 20 stickers.
- Live C3 from B → real mint; C4 live for the twin.
- Marketplace listing and buying working end to end.

- [ ] First AIRcoin minted from a live camera epoch (Gate 2)
- [ ] Mint visible in wallet and twin within 60 s of epoch close
- [ ] A listing created by the owner is bought by a second wallet

Phase 3 · Demo hardening

- Compliance burn, company portal and regulator portal.
- Cross-miner sticker duplicate check demoed with a second (virtual) miner.
- Explorer view linking each transaction to the testnet explorer; UI polish.
- Fallback: one script redeploys everything to a local chain and re-seeds demo wallets.

- [ ] Company buys and burns AIR; obligation bar fills; certificate shows the transaction hash
- [ ] Reused sticker rejected with a clear reason on the regulator portal
- [ ] Local-chain fallback brought up in under 5 minutes

Owns in the demo: steps 6–8 (sticker reuse, sell on the market, company burn).

10. Demo script, success metrics, risks and open questions

10.1 Demo script (about 8 minutes)

1. **The miner.** Show the physical rig, then the twin's 3D model; explode it to show camera, Pi, GPS and sensors. (A)
2. **It sees.** Live feed detects all 20 stickers; twin grid turns green; species labels appear. (A)
3. **It works.** Switch the scenario from clean morning to festival smog; mint rate rises on the ticker. (B)

4. **Remove a plant.** Pull one pot; its slot greys out within 10 s and the next epoch mints less. (A + B)
5. **Fake plant.** Put the plastic plant with a valid sticker in the slot; flagged as suspect, earns nothing. (A + B)
6. **Reuse a sticker.** A second virtual miner submits a proof with one of our sticker IDs; the validator rejects it and the regulator portal shows why. (C)
7. **Sell.** The owner lists AIRcoin on the marketplace; a buyer wallet purchases it. (C)
8. **Burn.** A factory account buys and burns AIRcoin; its compliance bar fills and a burn certificate appears. (C)

10.2 Success metrics

Metric	Target
Sticker detection at rig distance	20 of 20, at least 95% of frames
Species classification (held-out rig photos)	at least 85% top-1
Removal detected	within 10 s
Fake plant flagged	at least 4 of 5 tries
Epoch close to coin visible in wallet	under 60 s
Mints without a valid signature	0
Continuous demo run	15 min, no restart

10.3 Risks and fallbacks

Risk	Impact	Fallback
Fake-plant detection unreliable with an RGB camera	Anti-cheat claim weak	Use NoIR + NDVI; else add the fake class and a temporal check, and keep a pre-recorded clip
Pi too slow for vision	Low frame rate, late events	Run inference on a laptop with the same C1 output
Testnet RPC or faucet down on demo day	No live minting	One-script local-chain redeploy with seeded wallets

Risk	Impact	Fallback
Judges question the pollution numbers	Credibility	Present them as calibrated estimates, show the enclosure protocol and literature sources; avoid exact claims
Venue Wi-Fi unreliable	Proofs not delivered	Phone hotspot; offline queue in the miner
Plants damaged in transit	Fewer than 20 live plants	Carry spares; the demo works with fewer plants
Integration slips past Gate 2	No end-to-end story	Mocks stay runnable so each part still demos on its own
Token regulation questions	Pitch risk	Frame AIRcoin as a regulator-run compliance credit; legal review is out of scope

10.4 Open questions

- [ ] Hackathon deadline and total days available, to date the three phases
- [ ] Who takes which workstream
- [ ] Final list of 20 species and the literature behind each coefficient
- [ ] Definition of 1 AIR (g PM2.5-equivalent, kg CO_2-equivalent, or a weighted index)
- [ ] Demo epoch length and time-acceleration factor
- [ ] Testnet choice: Polygon Amoy vs Sepolia
- [ ] Standard Camera Module 3 or NoIR (decides the fake-plant approach)
- [ ] Which sensors to physically include versus simulate only
